

FIG. 1

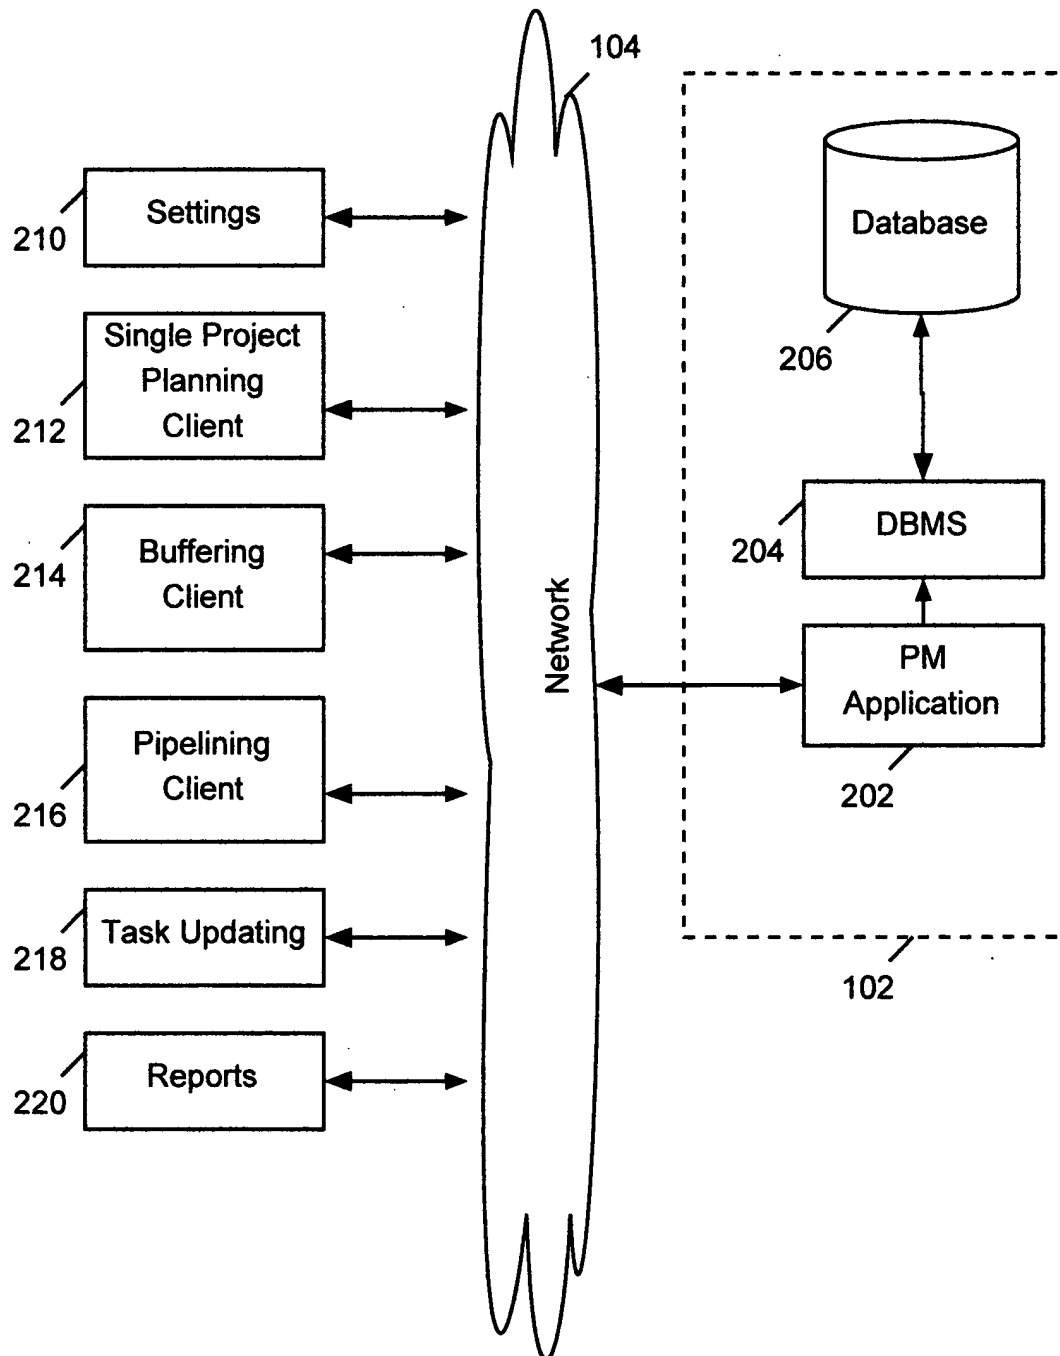


FIG. 2

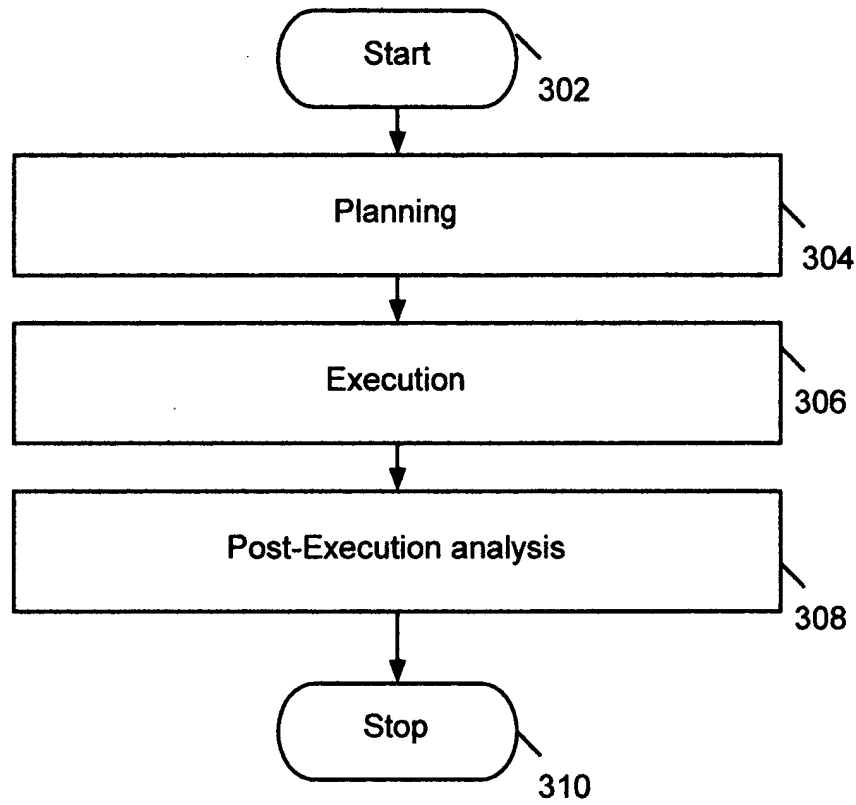


FIG. 3

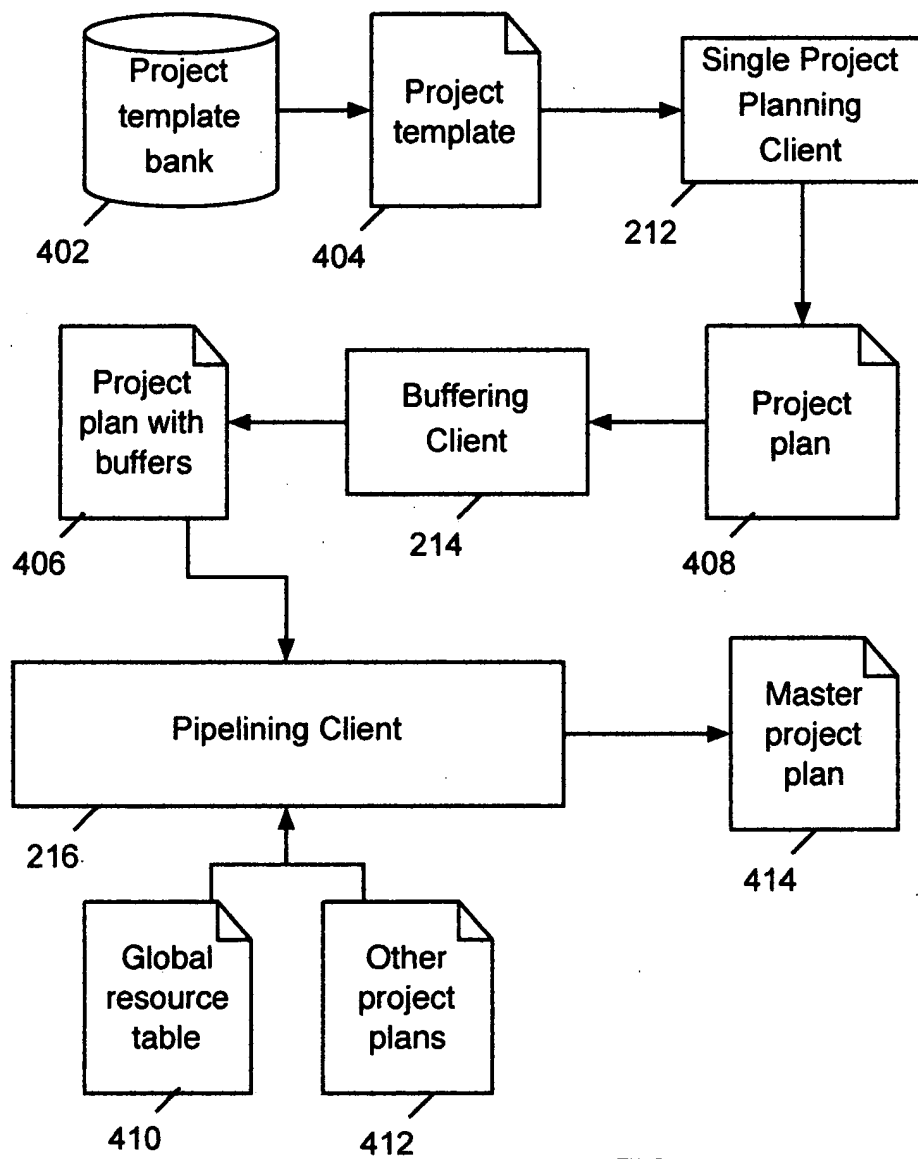


FIG. 4

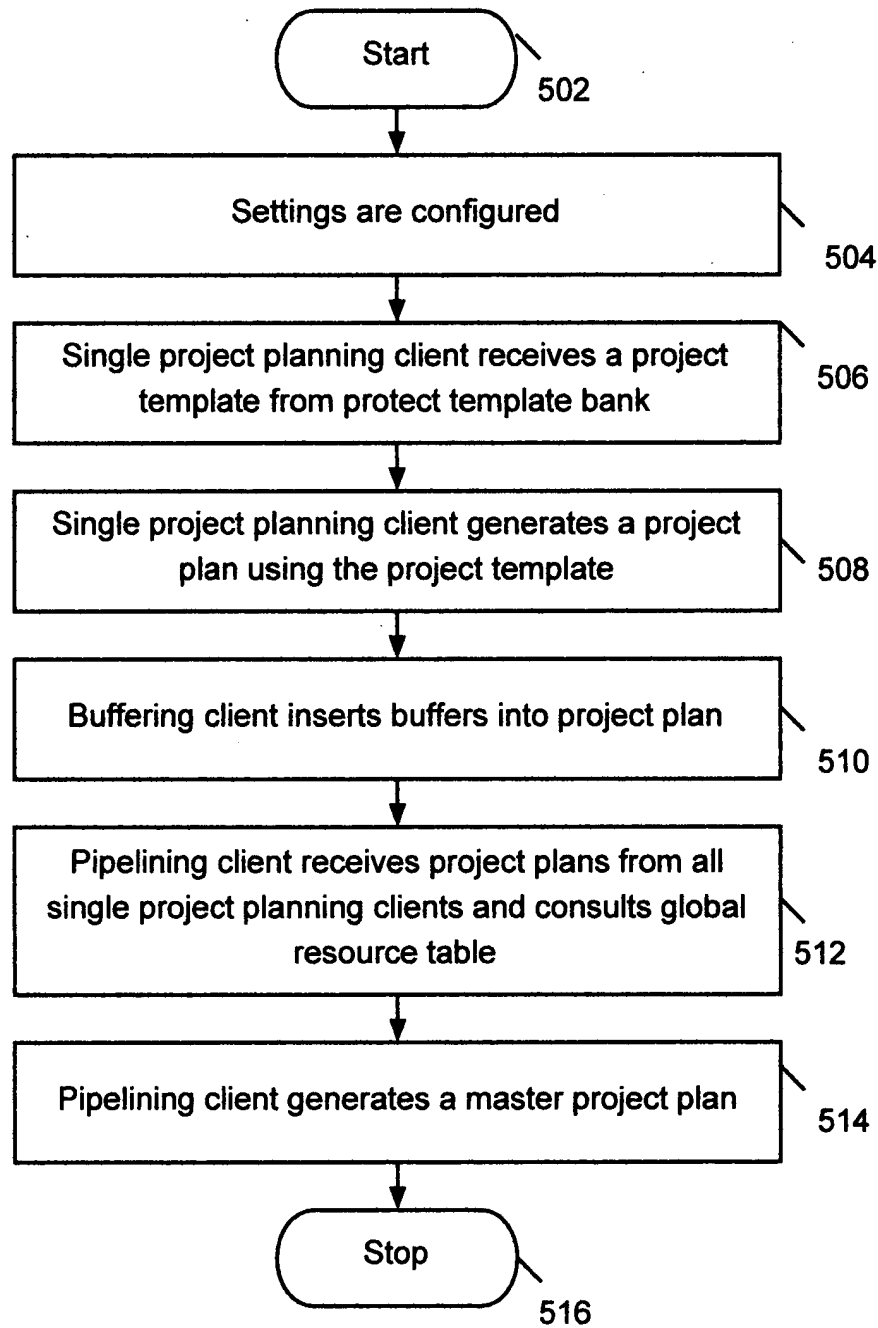


FIG. 5


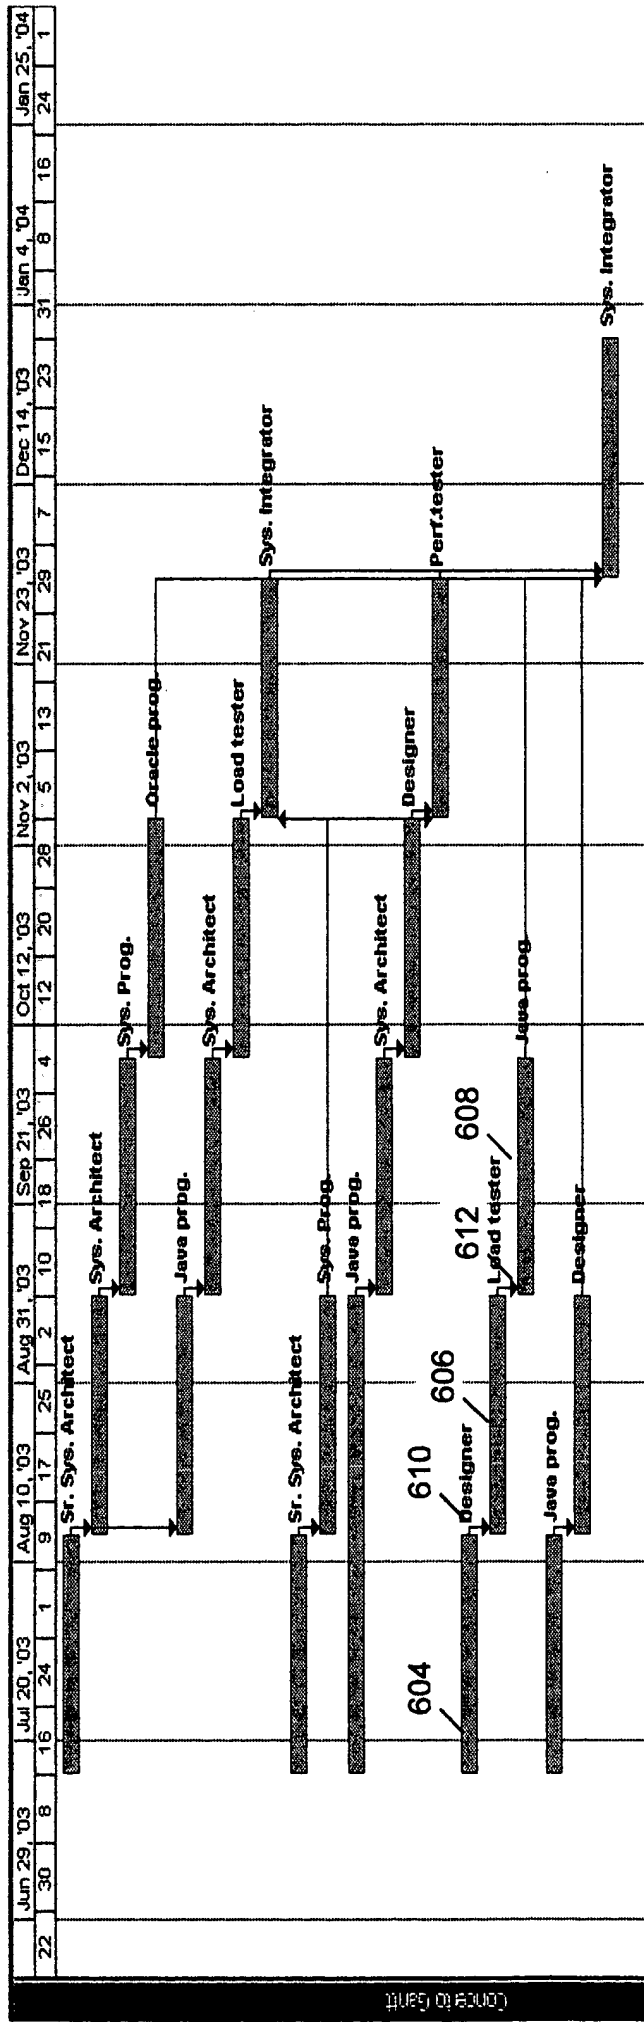


FIG. 6

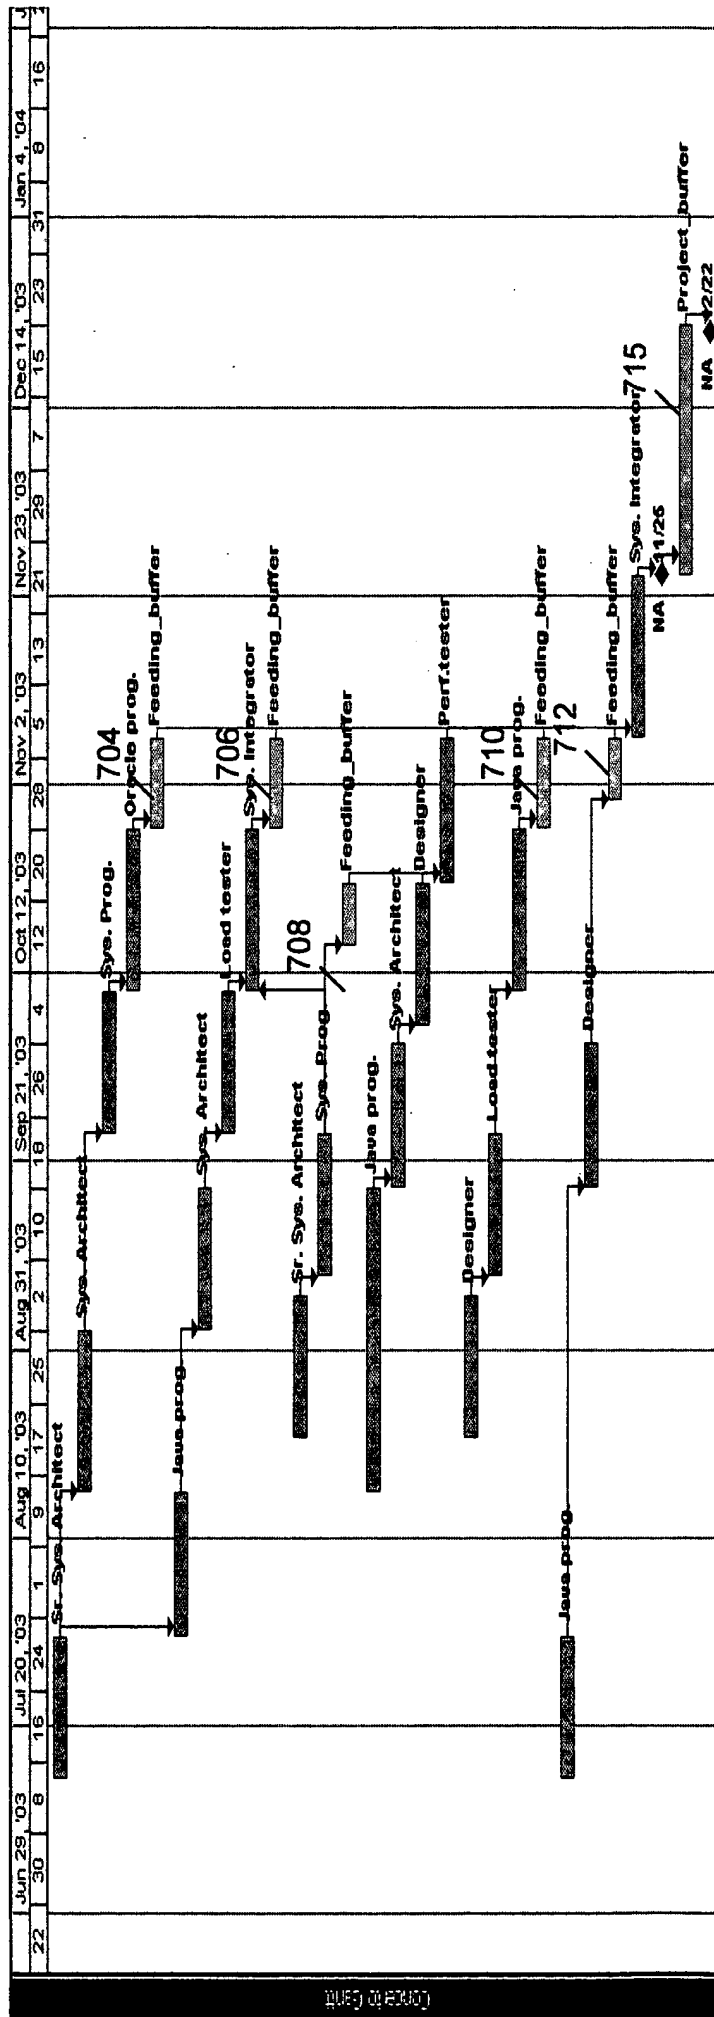

800

New Projects

puma_02 (02/20/2004)

Constraint(s): Diagnostic Engineer(3)

Project ID: puma_02

Project Manager: Mike Smith

Requested Date: 02/20/2004

☒ Use Remaining Buffer For DDQ

Projected Date: 03/26/2004

Set Projected Date

Penetration/Buffer Size: 25/124 (20 %) working days

Test Impact

Cycle Time Stretch (days): 24 working days

Accept Date

808

810

812

814

816

	Project	Fix	Priority	Orig. Rqst. Date	Due Date	Projected Date	Addl. Lateness	Cum. Lateness	Buffer Status
	cheetah_01	<input type="checkbox"/>	1	04/29/2003	04/29/2003	04/29/2003	0(0)	0(0)	14/124 (1)
	jag_1	<input type="checkbox"/>	2	05/09/2003	05/09/2003	05/09/2003	0(0)	0(0)	38/124 (3)
	puma_01	<input type="checkbox"/>	3	04/29/2003	04/29/2003	04/29/2003	0(0)	0(0)	38/124 (3)
	leopard_01	<input type="checkbox"/>	4	10/07/2003	10/07/2003	10/07/2003	0(0)	0(0)	0/124 (0)

↑ Capacity Allocation

↓ Priority


Fix
Unfix
Commit
Set Priorities
Test Impact
Accept Dates

FIG. 8



Resource Details

Number of Units : 3
Group : Hardware Test
Calendar : Standard

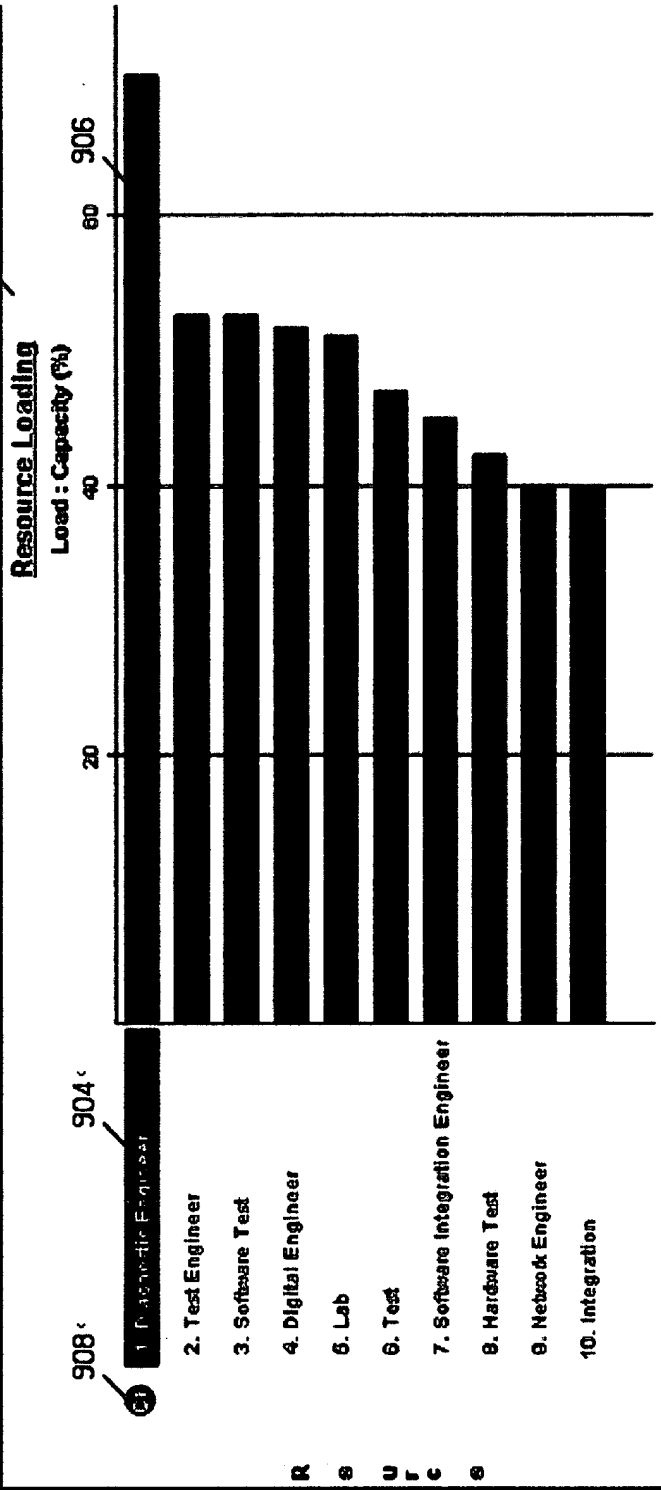

Project	Project Manager	Status
cheetah_01	Matti Herzberg	Regular
puma_01	Matti Herzberg	Regular
jag_1	Michael Smith	Regular
puma_02	Mike Smith	New
leopard_01	Tom Martin	Regular

FI . 9

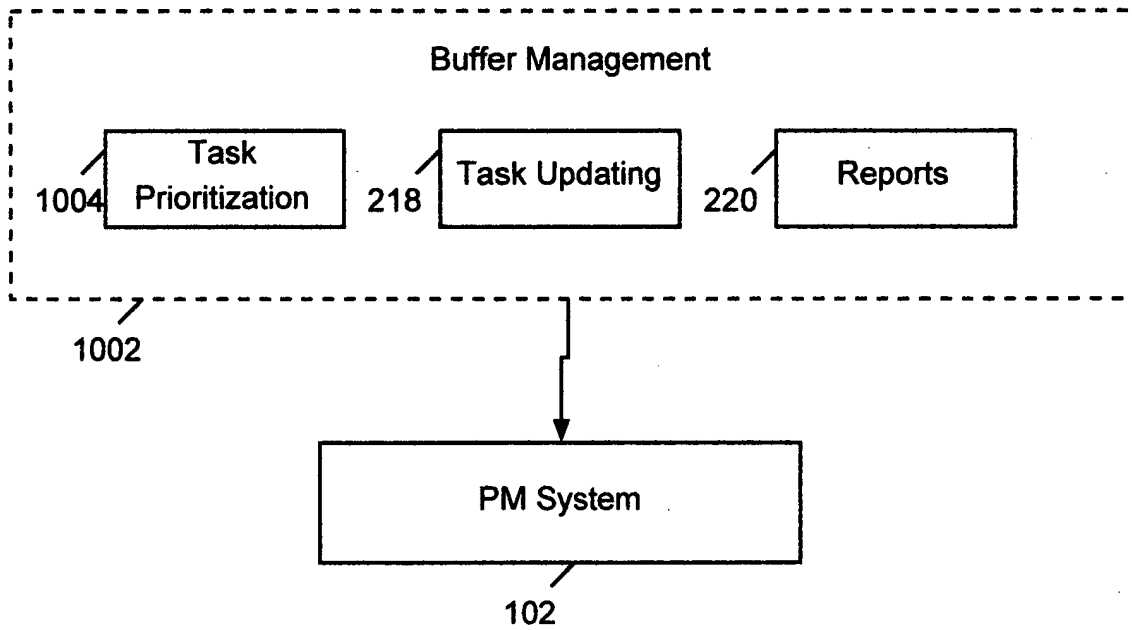


FIG. 10

Concerto 4.0 - Microsoft Internet Explorer provided by America Online

File Edit View Favorites Tools Help

Address <http://localhost/conweb/ITU.htm>

ConcertoWeb

Username: ResAdmin Server Name: concerto Change Password Log Out

Sys Admin Data Central Updates Execution Views Resource Portal P2P

Update Tasks | Assign Task Mgrs | Modify Projects | Add Project | Validate Project

Related Links:
Task Level Priorities By Task Mgr

Task Manager: Sanjeev Projects: All Projects 124
Start Date: 2/15/2002 + Days: 30 Define Sort

Task Type	Task Manager	Project Name	MSP Task ID	Task Description	Resource Notes	Earliest Arrival	Task Status	Actual Start Date	Actual End Date	Remaining Duration	Comments	No Change	Last Update Date
	Sanjeev	Cheetah_ver_01	27	F2/High Level/Review/Approve	Mike	2/15/2002	IP	2/13/2002		2d	Document re	<input type="checkbox"/>	2/15/2002
	Sanjeev	Cheetah_ver_01	31	F2/Module 1 LL Design		2/19/2002	NS			10d		<input type="checkbox"/>	
	Sanjeev	Puma_Ver_01	3	F1/High Level/Review/Approve	Jim	2/15/2002	IP	2/15/2002		10d	Customer ap	<input type="checkbox"/>	2/15/2002
	Sanjeev	Jaguar_01	29	F2/Data Design		2/15/2002	NS			10d		<input type="checkbox"/>	2/15/2002
	Sanjeev	Jaguar_01	27	F2/High Level/Review/Approve		2/26/2002	NS			5d		<input type="checkbox"/>	2/3/2002

1106 1110 1108 1112 1114

Page 1 Of 1

Validate

FIG. 11

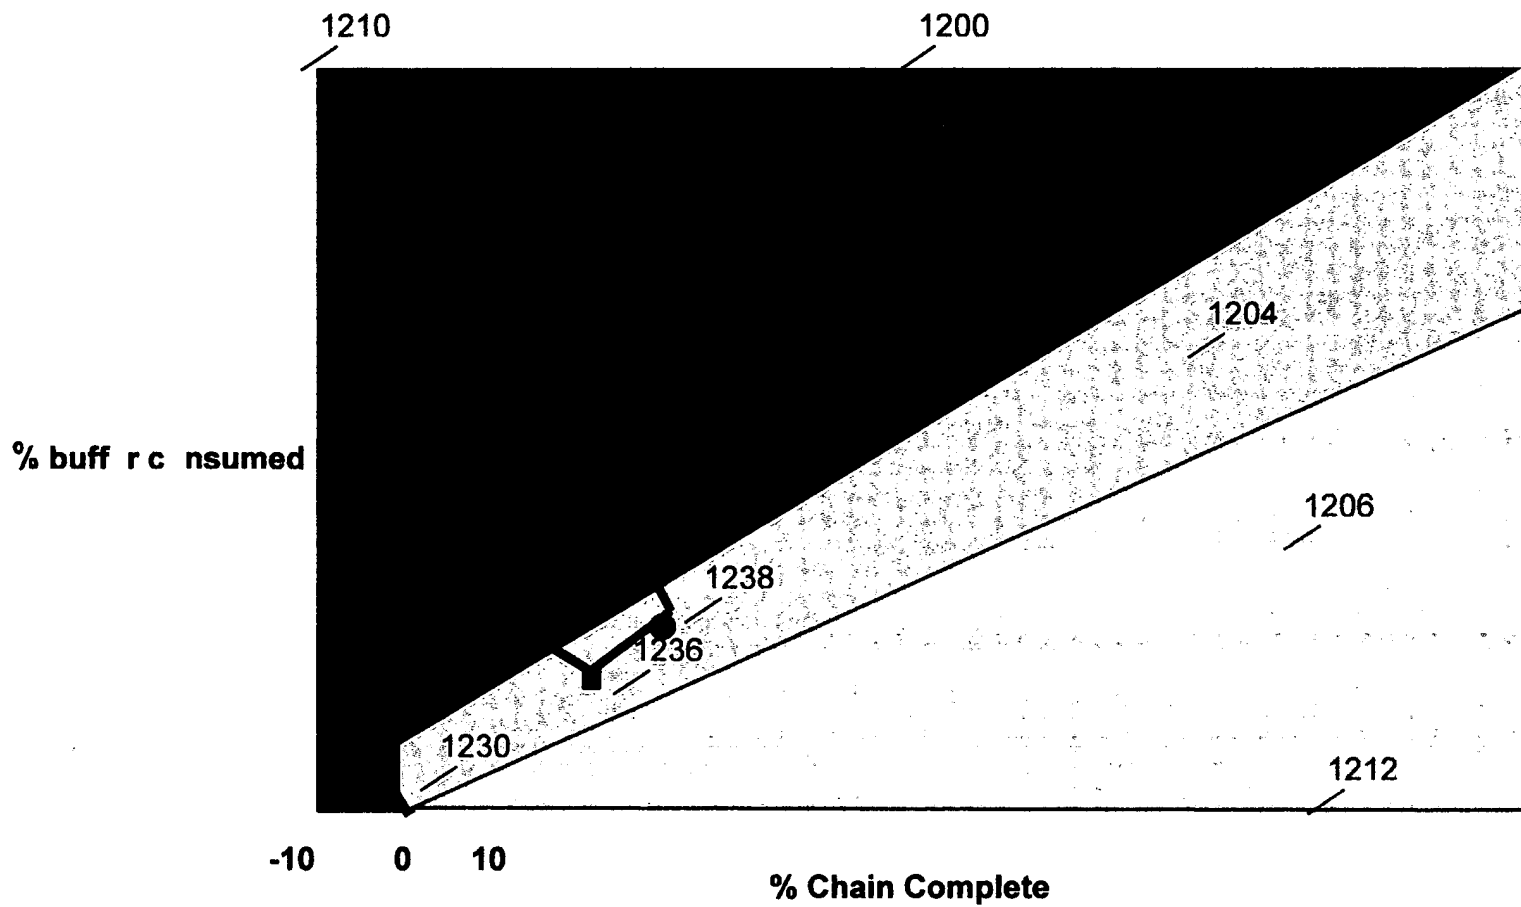


FIG. 12

1300

ConcertoWeb

Username: ResAdmin Server Name: concerto Change Password Log Out

Sys Admin Data Central Updates Execution Views Resource Portal P2P

Portfolio Status | Project Control | P2P Control | Task Level Priorities By: Task Mgr | Resource | Project

Task Manager: Sanjeev 1322

Projects: All Projects 1324

Start Date: 2/15/2002 + Days: 30

Print Preview
Export to Excel
Advanced Sort

Create Report

Project Name	MSP Task ID	Task Description	Task Mgr	Task Status	Resource Notes	Earliest Arrival	Remaining Duration	% CCCC Pen	% CMSB Pen	% CCFB Pen	Last Update Date	Ready To Start	Comments
1332 Puma Ver 01	3	E1/High Level/Review/Approve	Sanjeev	IP	Jim	2/15/2002 10d	31	47	100	100	2/15/2002	Customer approval in	
Cheetah ver 01 27		E2/High Level/Review/Approve	Sanjeev	IP	Nike	2/15/2002 2d	10	17	100	100	2/15/2002	Document revised for	
Jaguar 01	29	F2/Data Design	Sanjeev	NS		2/15/2002 10d	9	17	100	100	2/15/2002	Y	
Cheetah ver 01 31		F2/Module 1 UL Design	Sanjeev	NS		2/19/2002 10d	10	17	100	100		N	
Jaguar 01 1334	27	F2/High Level/Review/Approve	Sanjeev	NS		2/26/2002 5d	25	39	100	100	2/3/2002	Y	

FIG. 13A

Task Lev 1 Prioriti s By Pr ject - Chain View
1370

Project Manager: Matti Herzberg

Project :

Puma_Ver_01 1372 1374

Start Date:

2/15/2002 + Days: 30



Task Status		
<input checked="" type="checkbox"/> Not Started	<input checked="" type="checkbox"/> In Progress	<input type="checkbox"/> Completed

1364

1360 1358

1356

1380

Create Report

Project Name	MSP Task ID	Task Description	Task Mgr	Task Status	Earliest Arrival	Remaining Duration	% CCCB Pen /	% CMSB Pen	% CCFB Pen	Last Update Date	Ready To Start	Comments
Puma Ver 01 3		FL/High Level/Review/Approve	Sanjeev IP		2/15/2002	10d	31	47	100	2/15/2002		Customer approval in
Puma Ver 01 8		F1/Module 2 LL Design	Sridhar NS		3/1/2002	10d	31	47	100		N	
Puma Ver 01 32		F2/Module 3 LL Design	Sridhar NS		3/15/2002	20d	31	47	100		N	
Puma Ver 01 11		F1/Module 3 LL Design	Sridhar NS		3/1/2002	12d	20	32	100		N	
Puma Ver 01 5		F1/Module 1 LL Design	Sridhar NS		3/1/2002	15d	20	32	100		N	
Puma Ver 01 27		F2/High Level/Review/Approve	Mutu NS		2/15/2002	5d	19	29	100	2/3/2002	Y	
Puma Ver 01 22		F2/Data Design	Mutu IP		2/15/2002	10d	16	25	100	2/15/2002		
Puma Ver 01 4		F1/Data Design	Mutu NS		3/1/2002	15d	16	25	100		Y	
Puma Ver 01 35		F2/Module 2 LL Design	Sridhar NS		2/22/2002	2d	15	24	100	2/3/2002	N	
Puma Ver 01 31		F2/Module 1 LL Design	Sridhar NS		2/26/2002	10d	15	24	100		N	
Puma Ver 01 32		F2/Module 1 SW Coding	Rao NS		3/12/2002	7d	15	24	100		N	
Puma Ver 01 53		Phase 1 Hardware Design	Shai IP		2/15/2002	2d	5	10	100	2/15/2002		
Puma Ver 01 54		Phase 1 Hardware Development	Mark IP		2/19/2002	1d	5	10	100	2/15/2002		
Puma Ver 01 55		Phase 1 Components Fabrication	Guy NS		2/20/2002	8d	5	10	100	11/3/2001	N	
Puma Ver 01 58		Phase 1 Assembly	Guy NS		3/4/2002	2d	5	10	100	2/16/2002	N	
Puma Ver 01 59		Phase 1 Test	Paul NS		3/6/2002	10d	5	10	100		N	
Puma Ver 01 57		Phase 1 Test Development	Paul NS		2/20/2002	8d	4	8	100		N	

Done

Local intranet

FIG. 13B

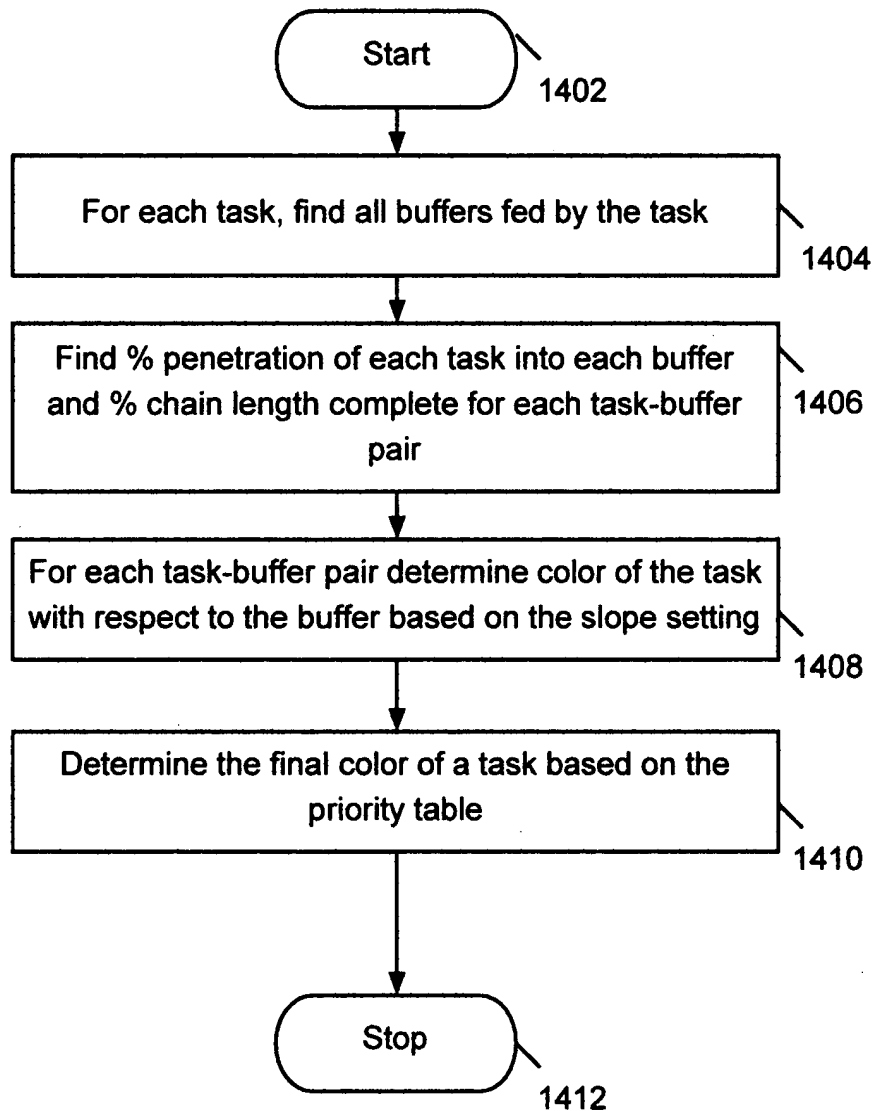


FIG. 14

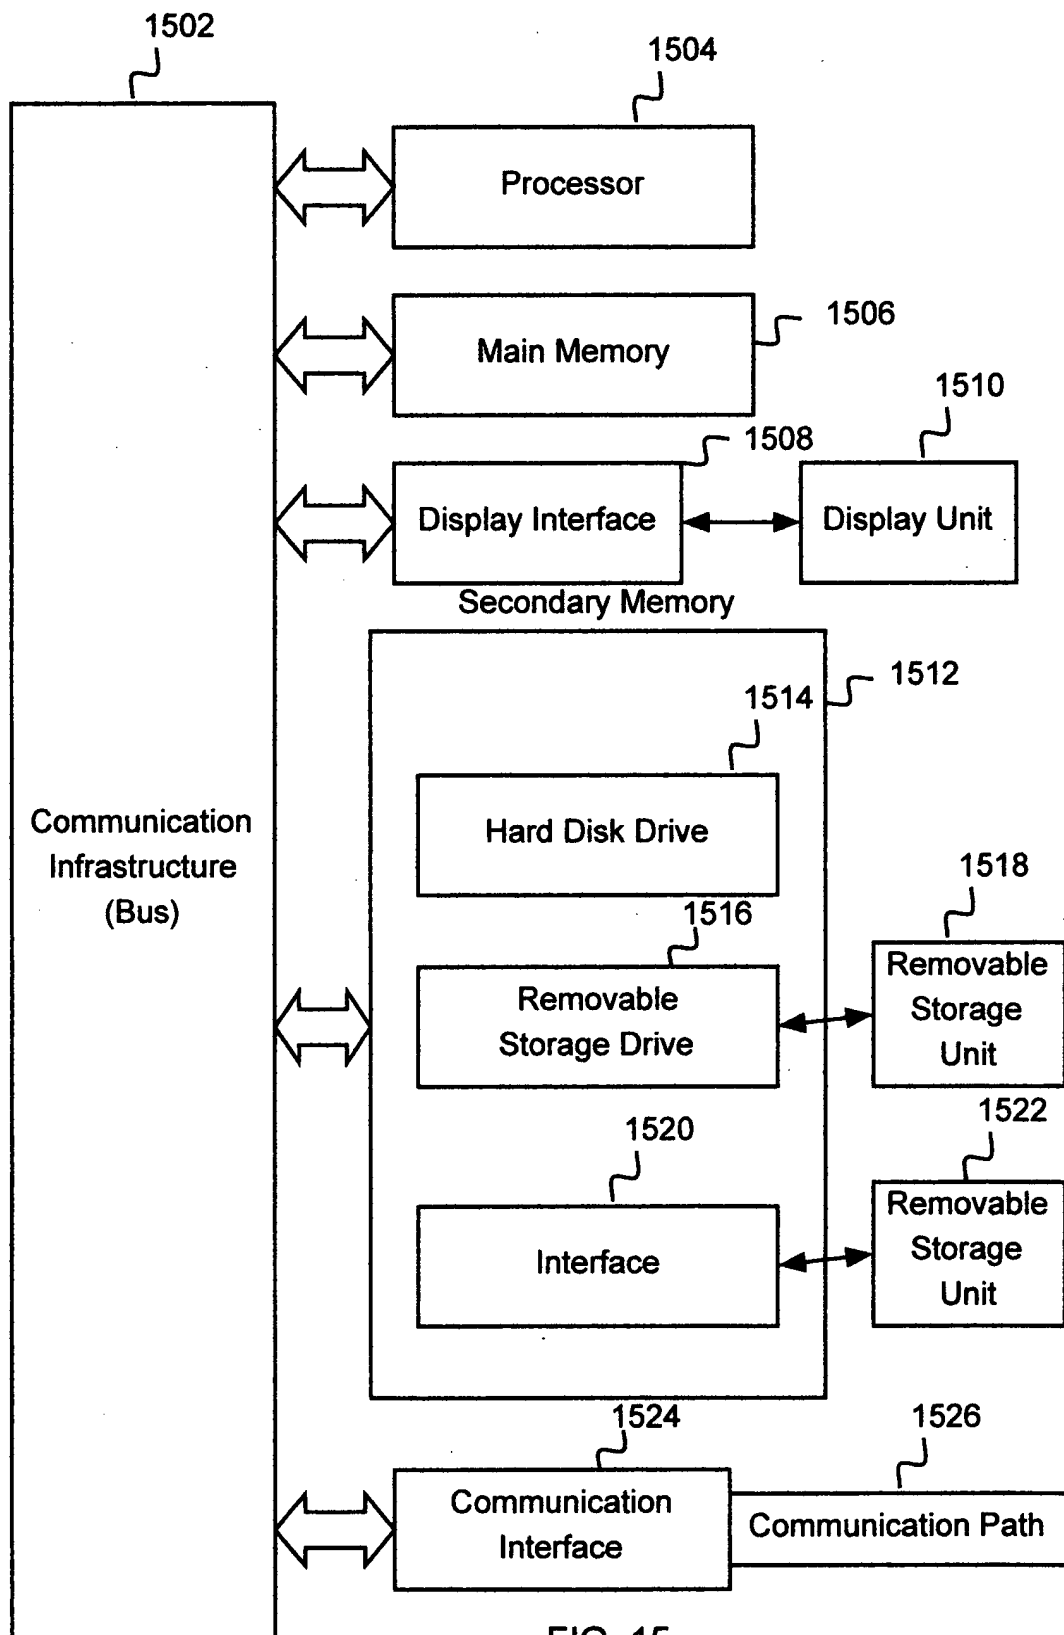


FIG. 15
